

Monthly Report March 2021

Dr. Thomas E. Randle High School & Harry Wright Junior High School

FM 2977 improvements are in progress.

Interior finishes are in progress.

Schools are on schedule to open in August 2021.



Transportation Fuel Tank Replacement

Morris & Associates is the Firm of Record.

New system is fully operational.

Soil remediation testing is on the Board Agenda.



Jane Long Historic Gym Renovations

VLK is the Architect of Record.

Canopies have been installed.

HVAC is operational.

Finishes are in progress.



ALC/1621 Additions and Renovations

VLK is the Architect of Record.

Masonry and roofing are in progress.

Junior High building has been demolished.



Lamar CHS & Lamar JHS Additions & Renovations

PBK is the Architect of Record.

High School. Former Admin Area painting is in progress. LGI will be turned over after Spring Break.

Junior High. Choir/Orchestra finishes are in progress. Parent Drive canopies are installed.

North Athletics Site. Roofing and exterior sheathing are in progress.

Traylor Stadium. Visitor locker room foundation is in progress.



Terry HS & George JHS Additions & Renovations

VLK Architects is the Architect of Record.

Terry. Band Hall & Multi-Purpose Room HVAC units will be installed during Spring Break.

George. Band Hall masonry and roof are in progress. Forum stage renovations will begin during Spring Break.



Multi-Purpose Room (HS) & Orchestra (MS) Additions

PBK is the Architect of Record.

Multi-Purpose Rooms. Foster, Fulshear, and George Ranch construction is in progress.

Orchestra Rooms. Navarro, Ryon Wertheimer, and Wessendorff construction is in progress.



Brazos Crossing Exterior Improvement

VLK is the Architect of Record.

Final payment recommendation is scheduled for the April Board Meeting.



Fletcher Morgan, Jr. Elementary School

VLK is the Architect of Record.

Piers, grade beams, and steel are in progress.


Site paving is 85% complete.



Maxine Phelan Elementary School

VLK is the Architect of Record.

Contractor recommendation is scheduled for the April Board Meeting.

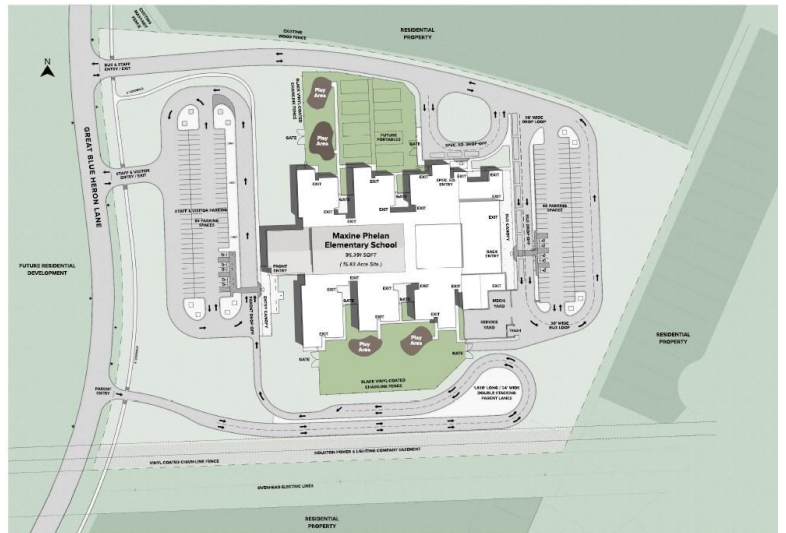

2017 BOND REFERENDUM SUMMARY					
PROJECT NAME	ORIGINAL BUDGET	BUDGET CHANGE	PROJECT BUDGET	COMMITTED	BALANCE
Roberts Middle School Orchestra Room	\$1,100,000.00	\$0.00	\$1,100,000.00	\$1,100,000.00	\$0.00
Austin ES Re-Roof	\$1,900,000.00	(\$529,504.00)	\$1,370,496.00	\$897,273.00	\$473,223.00
Seguin ECC Re-Roof	\$1,900,000.00	\$0.00	\$1,900,000.00	\$982,961.00	\$917,039.00
Terry HS Serving Lines	\$680,000.00	\$0.00	\$680,000.00	\$656,123.95	\$23,876.05
George JHS Serving Lines	\$620,000.00	\$0.00	\$620,000.00	\$528,728.39	\$91,271.61
Classroom Intruder Locks	\$400,000.00	\$0.00	\$400,000.00	\$390,985.72	\$9,014.28
High School LOTE Lab Renovations- Lamar / Terry / Foster	\$1,050,000.00	\$0.00	\$1,050,000.00	\$198,565.00	\$851,435.00
ES Cooler/Freezer Replacement - Austin / Bealsley / Huggins / Pink / Seguin / Taylor Ray / Travis / Williams	\$1,400,000.00	\$0.00	\$1,400,000.00	\$1,230,756.00	\$169,244.00
Summer 2019 Multi-Campus Improv. - Campbell ES Carpet / Campbell ES VWC / Navarro MS Carpet / Navarro MS Intercom / Wessendorff MS Carpet / Wessendorff MS VWC / Williams ES Carpet / Williams Admin. Renov. / Williams ES Fire Sprinklers	\$2,740,000.00	\$114,000.00	\$2,854,000.00	\$2,824,511.64	\$29,488.36
HS Field Turf & Foster HS Track - GR Turf / Fulshear Turf / Foster Turf / Terry Turf / Foster Track	\$9,082,719.00	\$0.00	\$9,082,719.00	\$7,352,923.72	\$1,729,795.28
Foster HS Athletic Improvements- HS Baseball & Softball Improv. / HS Field House Locker Replacement	\$867,281.00	\$0.00	\$867,281.00	\$829,768.00	\$37,513.00
Dr. Thomas E. Randle High School- High School / Turf / Multi-Purpose Room	\$127,630,000.00	\$0.00	\$127,630,000.00	\$115,386,733.73	\$12,243,266.27
Harry Wright Junior High School	\$62,000,000.00	\$0.00	\$62,000,000.00	\$55,441,207.82	\$6,558,792.18
Lamar CHS & Lamar JHS Exterior Improvements - Traylor Visitor Locker Room / Sub-Varsity Field / HS Multi- Purpose Room Add/ Turf/ Improved Drainage, Parking & Sidewalks / Revised JHS Drop Off / JHS HVAC Upgrades	\$15,340,000.00	\$0.00	\$15,340,000.00	\$2,987,206.00	\$12,352,794.00
Lamar CHS & Lamar JHS Additions & Renovations - HS Admin Renov. / LGI Add / HS Expand Band Hall / JHS Choir Add / JHS Intercom Upgrade	\$8,480,000.00	\$0.00	\$8,480,000.00	\$2,278,678.00	\$6,201,322.00
Terry HS & George JHS Additions & Renovations- JHS Renovated Locker Room / JHS Band Add / JHS Visitor Parking Add / JHS Forum Renov. / HS replace Wood Football Bleacher / HS Exterior Door & Window Replacement / HS Band & Chior Add / HS Resurface Parking / HS Multi-Purpose Room	\$14,650,000.00	\$0.00	\$14,650,000.00	\$8,154,309.00	\$6,495,691.00
Traylor Stadium Press Box Replacement	\$2,800,000.00	\$1,632,000.00	\$4,432,000.00	\$4,343,843.00	\$88,157.00
New Alternative Learning Center	\$12,200,000.00	\$0.00	\$12,200,000.00	\$1,228,860.00	\$10,971,140.00
Jane Long ES Historical Gym Renovations	\$3,200,000.00	\$0.00	\$3,200,000.00	\$3,048,979.00	\$151,021.00
Jane Long Auditorium Seating	\$125,000.00	\$0.00	\$125,000.00	\$0.00	\$125,000.00
Transportation - Replace Underground Fuel Tank	\$900,000.00	\$415,504.00	\$1,315,504.00	\$1,308,014.00	\$7,490.00
HS Multi-Purpose Rooms & MS Orchestra Adds - Foster MP / GR MP / Fulshear MP / Narvarro Orch / Wessendorff Orch / Ryon Orch / Wertheimer Orch / Foster HS Add Parking	\$9,570,000.00	\$0.00	\$9,570,000.00	\$9,119,829.30	\$450,170.70
Multi-Campus Carpet Replacement - HS / Briscoe JHS / Jackson ES / Pink ES / Long ES Foster	\$2,310,000.00	\$0.00	\$2,310,000.00	\$2,168,225.00	\$141,775.00
Summer 2020 Multi-Campus ES Renovations - Austin Office Renov. / Bowie Add 25 Parking Spaces / Bowie Replace Entry Canopy / Bowie Serving Line Renov. / Bowie Enlarge Cafeteria / Jackson Drainage Improv. / Jackson Serving Line Renov. / Smith Renov. Courtyard / Ray Improv Drainage in Parking Lot / Controls Upgrade	\$3,370,000.00	\$0.00	\$3,370,000.00	\$3,155,402.00	\$214,598.00
Brazos Crossing Renovations	\$1,800,000.00	\$0.00	\$1,800,000.00	\$115,420.00	\$1,684,580.00
Morgan Elementary School	\$30,200,000.00	\$0.00	\$30,200,000.00	\$24,487,855.00	\$5,712,145.00
Maxine Phelan Elementary School	\$32,600,000.00	\$0.00	\$32,600,000.00	\$12,975.00	\$32,587,025.00
New Elementary School #31	\$35,200,000.00	\$0.00	\$35,200,000.00	\$0.00	\$35,200,000.00
Land	\$20,000,000.00	\$0.00	\$20,000,000.00	\$0.00	\$20,000,000.00
TOTAL	\$404,115,000.00	\$1,632,000.00	\$405,747,000.00	\$250,230,133.27	\$155,516,866.73
TOTAL FACILITY & PLANNING BOND	\$404,115,000.00	funded by 2014			
REMAINING FACILITY & PLANNING BOND	\$155,516,866.73	bond available			
		funds			

2017 BOND TECHNOLOGY SUMMARY					
PROJECT NAME	ORIGINAL BUDGET	BUDGET CHANGE	PROJECT BUDGET	COMMITTED	BALANCE
IFP-Interactive Flat Panel	\$9,044,000.00	\$0.00	\$9,044,000.00	\$7,996,136.00	\$1,047,864.00
PT0-Printer Refresh	\$1,440,000.00	\$0.00	\$1,440,000.00	\$1,347,355.18	\$92,644.82
CCU-Campus Core Uplink	\$740,000.00	\$0.00	\$740,000.00	\$737,976.00	\$2,024.00
ES0-Expanded Storage	\$400,000.00	\$0.00	\$400,000.00	\$400,000.00	\$0.00
SC0-Security Cameras	\$250,000.00	\$0.00	\$250,000.00	\$250,000.00	\$0.00
TEL-Telephones	\$890,000.00	\$0.00	\$890,000.00	\$747,671.96	\$142,328.04
CRO-Computer Refresh	\$18,344,000.00	\$0.00	\$18,344,000.00	\$16,271,655.00	\$2,072,345.00
LC0-Laptop Carts	\$450,000.00	\$0.00	\$450,000.00	\$0.00	\$450,000.00
SCN-Eduphoria Scanners	\$122,000.00	\$0.00	\$122,000.00	\$121,450.00	\$550.00
IA0-Interact	\$2,646,000.00	\$0.00	\$2,646,000.00	\$0.00	\$2,646,000.00
TOTAL	\$34,326,000.00	\$0.00	\$34,326,000.00	\$27,872,244.14	\$6,453,755.86
TOTAL TECHNOLOGY BOND	\$34,326,000.00				
REMAINING TECHNOLOGY BOND	\$6,453,755.86				

2017 BOND TRANSPORTATION SUMMARY					
PROJECT NAME	ORIGINAL BUDGET	BUDGET CHANGE	PROJECT BUDGET	COMMITTED	BALANCE
New Bus Purchase	\$5,175,000.00	(\$7,300.00)	\$5,167,700.00	\$2,560,746.00	\$2,606,954.00
Add Air to Buses	\$1,335,000.00	\$0.00	\$1,335,000.00	\$0.00	\$1,335,000.00
Smart Tag	\$500,000.00	\$7,300.00	\$507,300.00	\$507,250.91	\$49.09
TOTAL	\$7,010,000.00	\$0.00	\$7,010,000.00	\$3,067,996.91	\$3,942,003.09
TOTAL TRANSPORTATION BOND	\$7,010,000.00				
REMAINING TRANSPORTATION BOND	\$3,942,003.09				

